

Construction Project Briefing

May 10, 2017



Today's Presentation

- **95th Street Terminal Improvement Program**
- **Wilson Transfer Station, Track, and Structure Reconstruction**
- **Ravenswood Loop Signals Upgrade Project**
- **Illinois Medical District (IMD) Rehabilitation Project**
- **Quincy Loop Station Upgrade**



Project Title: 95th Terminal Improvement Program

Justification of Need:	The terminal is functionally obsolete and does not allow for optimal bus operations and pedestrian flow.
Priority of Project:	High
Total Project Budget:	\$280 M
Construction Contract Value:	Advance Package 1: \$ 2,482,588 Advance Package 2: \$24,697,210 Main Terminal Contract: \$180,000,000
Earned to Date:	Advance Package 1: 100% Advance Package 2: 96% Main Terminal Contract: 17%
Percent Change Orders to Construction Contract:	Advance Package 1: (0.3%) Advance Package 2: 7% Main Terminal Contract: 0%
Percent Time Used:	Advance Package 1: 100% Advance Package 2: 100% Main Terminal Contract: 47%
DBE:	Advance Package 1: Goal: 30% / Commitment: 35.19% / Current Attainment*: 37.26% Advance Package 2: Goal: 30% / Commitment: 30% / Current Attainment*: 32.03% Main Terminal Contract: Goal: 27% / Commitment: 27% Outreach events conducted: 8 *Attainment is based on progress payments and may vary over the life of the project
Funding Source:	Federal, State, Bond



Project Title: 95th Terminal Improvement Program

Estimated Start Date/Estimated Length of Project:	Advance Package 1: NTP Issued June 6, 2014 / 180 days Advance Package 2: NTP Issued July 24, 2014 / 661 days Main Terminal Contract: NTP Issued Nov 24, 2015 / 1118 days
AP1/AP2 Construction Manager/General Contractor:	Walsh / II in One JV
Main Terminal Contractor:	F.H. Paschen / Milhouse JV
Owners Representative:	Jacobs/SQN JV

Detailed Overview of Scope:

The 95th Terminal Improvement Project will create new South and North terminal buildings at 95th on the Dan Ryan Red Line. The new terminal buildings will create a functional and efficient intermodal facility to enhance bus service and improve pedestrian safety. Scope includes the replacement and expansion of the terminal and platform and the addition of bus and pedestrian bridges. New administrative office space will be built and new bus bays will be provided around the terminal buildings.



Project Title: 95th Terminal Improvement Program

Impact on Customers:	Track closures and weekend station closures during construction. Temporary relocation of certain bus operations to nearby streets during construction phasing.
Benefit to System:	Improved customer circulation and safety by relieving congestion. Improved bus service and improved pedestrian safety.
Benefit to Community:	Improved pedestrian safety with new pedestrian bridge over 95 th Street, longer train platform extending to the new South Terminal Building.
Impact on Accessibility:	New south and north terminal buildings with improved accessible routes to buses.
Estimated # of Jobs Created:	3,120 (Direct, Indirect and Induced), 652 (Direct)
Customer Communication Need:	Requires periodic track closures and possible station closures with bus shuttle service. Bus Operations may be relocated to adjacent streets during certain phases of construction.

Comparable Projects:
<ul style="list-style-type: none"> Wilson Station



Project Title: 95th Terminal Improvement Program

Construction Progress

Phase	Description	Status
<p>Close-out Advance Package 2: Dan Ryan Retaining Walls</p> <p>Design/ Pre-Construction Main Terminal Contract</p> <p>Construction Main Terminal Contract</p>	<ul style="list-style-type: none"> ▪ CTA issued Substantial Completion for Milestone 2 on May 15, 2016. ▪ Administrative close-out is ongoing. ▪ Design progression on Design Package 5: North Terminal is ongoing. ▪ Contractor is evaluating various Trade Work Package bids, such as Storefront & Curtainwall, Building Electrical & Communications, South Terminal Interior Building Trades, and Traffic Signals. ▪ Bid solicitation is ongoing for Building & Site Signage. ▪ The following Concurrence of Award (COA) were executed: <ul style="list-style-type: none"> ▪ COA-11: HVAC, Masonry, Site Concrete & Rebar, Granite Flooring, Site Demo & Excavation, Platform & Station Concrete & Rebar. ▪ Construction of west side track completed. ▪ Demolition of east side track, traction power and underground ductbanks completed. Mass excavation of east side track area completed. ▪ Platform barrier fence installed to isolate construction zone on east side track area. ▪ Relay house removed. ▪ East side barrier wall demolished. ▪ South bus bridge pier rebar and formwork installation in process. 	<p>Ongoing</p> <p>Ongoing</p> <p>Ongoing</p>
<p>Delay Explanation:</p>		
<p>N/A</p>		



Project Title: 95th Terminal Improvement Program



West Track Rebuilt, East Barrier Wall Demolition



Project Title: 95th Terminal Improvement Program



Barrier Wall Demo Complete, Caissons Installation Begins



Project Title: 95th Terminal Improvement Program



South Bus Bridge Pier Rebar and Formwork Installation



Project Title: 95th Terminal Improvement Program



Signal Relay House Removal



Project Title: Wilson Transfer Station, Track & Structure Reconstruction

Justification of Need:	The Station is functionally obsolete and does not allow for optimal transit operations.
Priority of Project:	High
Total Project Budget:	\$206 M
Construction Contract Value:	\$ 152,370,000
Earned to Date:	65%
Percent Change Orders to Construction Contract:	(0.7 %)
Percent Time Used:	79%
DBE:	Goal: 25% / Commitment: 27.52% Outreach events conducted: 1
Funding Source:	Federal, State, Bond and TIF
Estimated Start Date/Estimated Length of Project:	NTP 7/25/14; Substantial Completion 1/10/18
Designer of Record:	HNTB
Construction Manager/General Contractor:	Arcadis/Walsh/II In One JV

Detailed Overview of Scope: The station will replace the badly deteriorated station that was built in 1923. The station will have multiple entrances/exits and will include the following features:

- Two (2) new 26 foot – 10 car concrete island platforms with full canopies.
- New main station located on the south side of Wilson Ave., new auxiliary entrance/exit at Sunnyside Ave. and a new auxiliary entrance/exit on the north side of Wilson.
- New elevators, escalators, lighting, signage, fare control, security cameras and art work.
- Replace old existing elevated track structure with new track structure to accommodate the new station platform and the necessary infrastructure to support the new track alignment.



Project Title: Wilson Transfer Station, Track & Structure Reconstruction

Impact on Customers:	There will be minimum impact to CTA customers
Benefit to System:	<ul style="list-style-type: none"> • New modern, more spacious and accessible stationhouse with three (3) entrances. • Upgraded track structure infrastructure and signals for more reliable service. • New transfer point between Red and Purple express rail lines.
Benefit to Community:	<ul style="list-style-type: none"> • Modern facility with new system upgrades. • Easy access entrances through three (3) entry points. • Bigger platforms that will accommodate higher capacity for passengers to avoid overcrowding. • Platform canopies to protect customers from elements. • New ADA accessible station.
Impact on Accessibility:	Station will be fully accessible upon completion.
Estimated # of Jobs Created:	560
Customer Communication Need:	<ul style="list-style-type: none"> • Construction activity notices will be provided to inform businesses and residents regarding temporary stations and construction impacts (noise, dust, street/alley impacts) throughout the project.

Comparable Projects:

- 95th Station – Red Line



Project Title: Wilson Transfer Station, Track & Structure Reconstruction

Construction Progress

Phase	Description	Status
Construction	<ul style="list-style-type: none"> Track 4 steel structure demolition 90% completed. 	Ongoing
	<ul style="list-style-type: none"> Wilson main station build out continues. 	Ongoing
	<ul style="list-style-type: none"> Wilson auxiliary station build out continues. 	Ongoing
	<ul style="list-style-type: none"> Sunnyside west ramp steel structure and precast floor installation continues. 	Ongoing
	<ul style="list-style-type: none"> Caisson installation activities (30) for new track 4 - 70% completed. 	Ongoing
	<ul style="list-style-type: none"> Concrete foundation pedestals (30) installation continues – 50% completed. 	Ongoing
	<ul style="list-style-type: none"> Install new east elevator steel structure tower. 	Ongoing
	<ul style="list-style-type: none"> Leland embankment track 4 approach slab installation continues. 	Ongoing
	<ul style="list-style-type: none"> New track 4 steel structure installation continues. 	Ongoing
	<ul style="list-style-type: none"> Install new supervisor booth at east platform. 	Planned
	<ul style="list-style-type: none"> Start Sunnyside station excavation for new foundation and underground utilities. 	Planned

Delay Explanation:

N/A



Project Title: Wilson Transfer Station, Track & Structure Reconstruction



Track 4 Steel Demolition



Project Title: Wilson Transfer Station, Track & Structure Reconstruction



New Track 4 Caisson Drilling Operations



Project Title: Wilson Transfer Station, Track & Structure Reconstruction



Wilson Main Station Foundation Build Out



Project Title: Wilson Transfer Station, Track & Structure Reconstruction



New East Elevator Steel Tower Frame Installation



Project Title: Ravenswood Loop Signal Upgrade Project

Justification of Need:	The signal system for the Ravenswood Loop Connector section of the CTA Brown line was originally commissioned in 1975. In order to decrease headways and improve reliability, the system will be replaced with a new system.
Priority of Project:	High
Total Project Budget:	\$ 50 M
Construction Contract Value:	\$ 32.6M
Earned to Date:	29.37%
Percent Change Orders to Construction Contract:	0
Percent Time Used:	67.1%
DBE:	Goal: 10% / Commitment: 10% Outreach events conducted: 1 (CTA)
Funding Source:	CTA PBV, CTA Bonds, FTA
Start Date/Length of Project:	November 4, 2015 – January 3, 2018
Designer of Record:	Parsons Transportation
Construction Manager/General Contractor:	Parsons Brinckerhoff/Ragnar Benson Construction, LLC

Overview of Scope: The signal system upgrade will include the following features:

- Removal of all existing signal equipment, cabling, and signal platforms.
- Design & install new platforms, cabling, cable support brackets, and signal equipment.
- Communication network design, configuration, installation, and commissioning.



Project Title: Ravenswood Loop Signal Upgrade Project

Impact on Customers:	54 hour line cut to cut over new signal system.
Benefit to System:	<ul style="list-style-type: none"> • Decreased headways • More reliable equipment • More robust signal network • Better diagnostic abilities • More reliable track circuit indications • Added loss of shunt detection system • Optimized curve speeds (potentially reduce run times)
Benefit to Community:	<ul style="list-style-type: none"> • Maximizing number of trains allowed in the corridor. • Less customer inconvenience due to signal system malfunction.
Impact on Accessibility:	None
Estimated # of Jobs Created:	89
Customer Communication Need:	<ul style="list-style-type: none"> • Construction activity notices will be provided to inform businesses and residents regarding line cut and construction impacts (noise, dust, street/alley impacts) throughout the project.

Comparable Projects:
<ul style="list-style-type: none"> • Loop Signal Project • Dearborn Signal Project



Project Title: Ravenswood Loop Signal Upgrade Project

Construction Progress

Phase	Description	Status
Construction	<ul style="list-style-type: none"> • Installation of cable brackets and cable. 	Ongoing
	<ul style="list-style-type: none"> • Installation of foundations and structural steel to support new signal houses. 	Ongoing
	<ul style="list-style-type: none"> • Installation of new signal houses. 	Planned
	<ul style="list-style-type: none"> • Installation of new signal equipment. 	Planned
	<ul style="list-style-type: none"> • Integration and troubleshooting of new system. 	Planned
	<ul style="list-style-type: none"> • System Cutover. 	Planned

Delay Explanation:
N/A



Project Title: Ravenswood Loop Signal Upgrade Project



Installation Signal House Platform Steel at Cleveland



Project Title: Ravenswood Loop Signal Upgrade Project



Installation Signal House Platform Steel at Cleveland



Project Title: Illinois Medical District (IMD) Rehabilitation Project

Justification of Need:	To improve the accessibility of the Illinois Medical District Station and rehabilitate the station to a state of good repair. The project will make all three station entrances ADA accessible, including the addition of an elevator to the Ogden entrance.
Priority of Project:	High
Total Project Budget:	\$23 M
Construction Contract Value:	\$14,221,000
Earned to Date:	7%
Percent Change Orders to Construction Contract:	0%
Percent Time Used:	48%
DBE:	Goal: 30%, Commitment: 30% Outreach events conducted: 2 (CTA)
Funding Source:	TIF
Estimated Start Date/Estimated Length of Project:	NTP: September 26, 2016 Substantial Completion : January 26, 2018
General Contractor:	McHugh Construction/ UJAMAA Joint Venture
Construction Manager / Owners Representative:	STV

Detailed Overview of Scope:

The Illinois Medical District Rehabilitation Project will rehabilitate the Damen and Paulina stationhouses and concourses through structural reinforcements and upgraded exterior envelopes & interior improvements. The project will reconstruct and expand the Ogden stationhouse providing new upgraded electrical service and elevator access to the platform as well as reinforced structural components. Platform restorations and improvements will also be incorporated. All three station entrances will be ADA compliant and will incorporate lighting improvements, communication system improvements and signage upgrades.



Project Title: Illinois Medical District (IMD) Rehabilitation Project

Impact on Customers:	<p>Station will remain open at all times. Temporary Station Entrance closures will occur and access to portions of the platform will be limited during phased construction work. ADA accessibility will be maintained at either the Paulina Stationhouse or Damen Stationhouse during all phases of construction.</p> <ul style="list-style-type: none"> • 50 maximum nightly single track occurrences. • 5 maximum weekend single track occurrences. • Partial platform closures
Benefit to System:	Improved customer circulation. Provides accessibility to customers with disabilities at all 3 entrances of IMD Station which maintains the highest ridership on the Congress Branch.
Benefit to Community:	Improved aesthetics and pedestrian safety with new metal panel stationhouse exteriors, stainless steel stationhouse interior panels & new stationhouse storefronts. Upgraded LED lighting, upgraded communication systems and new signage.
Impact on Accessibility:	New elevator installation at Ogden Stationhouse. Concrete resurfacing of Damen & Paulina Concourses.
Estimated # of Jobs Created:	63
Customer Communication Need:	Construction activity notices will be needed to alert customers, businesses and residents to temporary entrance closures, weekend and night work occurrences. Extensive communication will be required for weekend closures and for extended partial platform closures.

Comparable Projects:
<ul style="list-style-type: none"> • Quincy Loop Station Upgrade • YNB 5-Stations Project



Project Title: Illinois Medical District (IMD) Rehabilitation Project

Construction Progress

Phase	Description	Status
Construction	<ul style="list-style-type: none">▪ Paulina Temp ADA Accessibility Work.▪ Damen Entrance Closure for Rehabilitation.▪ Damen Stationhouse Rehabilitation.▪ Damen Concourse Rehabilitation.▪ Partial Platform Rehabilitation.▪ Review of Submittals and Process Plans.▪ Damen Stationhouse Reopening.▪ Ogden / Paulina Entrance Closure for Rehabilitation.	Complete Complete Ongoing Ongoing Ongoing Ongoing Planned Planned

Delay Explanation:

N/A



Project Title: Illinois Medical District (IMD) Rehabilitation Project



Damen Stationhouse Tuckpointing



Project Title: Quincy Loop Station Upgrade

Justification of Need:	The Station is not currently accessible. The project will provide another accessible Loop station, as well as provide additional repairs and improvements throughout the station.
Priority of Project:	High
Total Project Budget:	\$ 18M
Construction Contract Value:	\$ 11.7M
Earned to Date:	10%
Percent Change Orders to Construction Contract:	0
Percent Time Used:	57%
DBE:	Goal: 30%, Commitment: 30% Outreach events conducted: 1 (CTA)
Funding Source:	TIF, CTA Bonds
Estimated Start Date/Estimated Length of Project:	NTP 7/27/16 ; Substantial completion 12/24/17
Designer of Record:	Exp US Services
Construction Manager/General Contractor:	Parsons Brinckerhoff/Ragnar Benson Construction, LLC

Detailed Overview of Scope: The station will include the following features:

- Two (2) new Elevators with connection bridges to stationhouses.
- One new exit stair.
- New electrical service.
- New and upgraded Electrical fixtures
- Painting upgrades
- Replacement of existing wood floors with new tile floors at both stationhouses



Project Title: Quincy Loop Station Upgrade

Impact on Customers:	There will be minimum impact to CTA customers.
Benefit to System:	<ul style="list-style-type: none"> • Accessible Station. • New upgraded electrical service to the station. • Upgraded lighting. • New stationhouse floors.
Benefit to Community:	<ul style="list-style-type: none"> • It will improve beneficial use of the station by providing accessible path to the station. • Easy access entrances through two new (2) entry points. • New outer loop platform exit stair will provide a new exit point from platform to street.
Impact on Accessibility:	Station will be fully accessible upon completion.
Estimated # of Jobs Created:	150
Customer Communication Need:	<ul style="list-style-type: none"> • Construction activity notices will be provided to inform businesses and residents regarding temporary stations and construction impacts (noise, dust, street/alley impacts) throughout the project.

Comparable Projects:
<ul style="list-style-type: none"> • IMD Station – Blue Line



Project Title: Quincy Loop Station Upgrade


Construction Progress

Phase	Description	Status
Construction	<ul style="list-style-type: none">• The south east stair has been removed to be refurbished.	Completed
	<ul style="list-style-type: none">• Contractor mobilized to the site and completed construction fence installation.	Completed
	<ul style="list-style-type: none">• Installation of new temporary street lighting continues.	Ongoing
	<ul style="list-style-type: none">• Earth Retention System (ERS) and micropile installation to begin.	Planned

Delay Explanation:
N/A



Project Title: Quincy Loop Station Upgrade

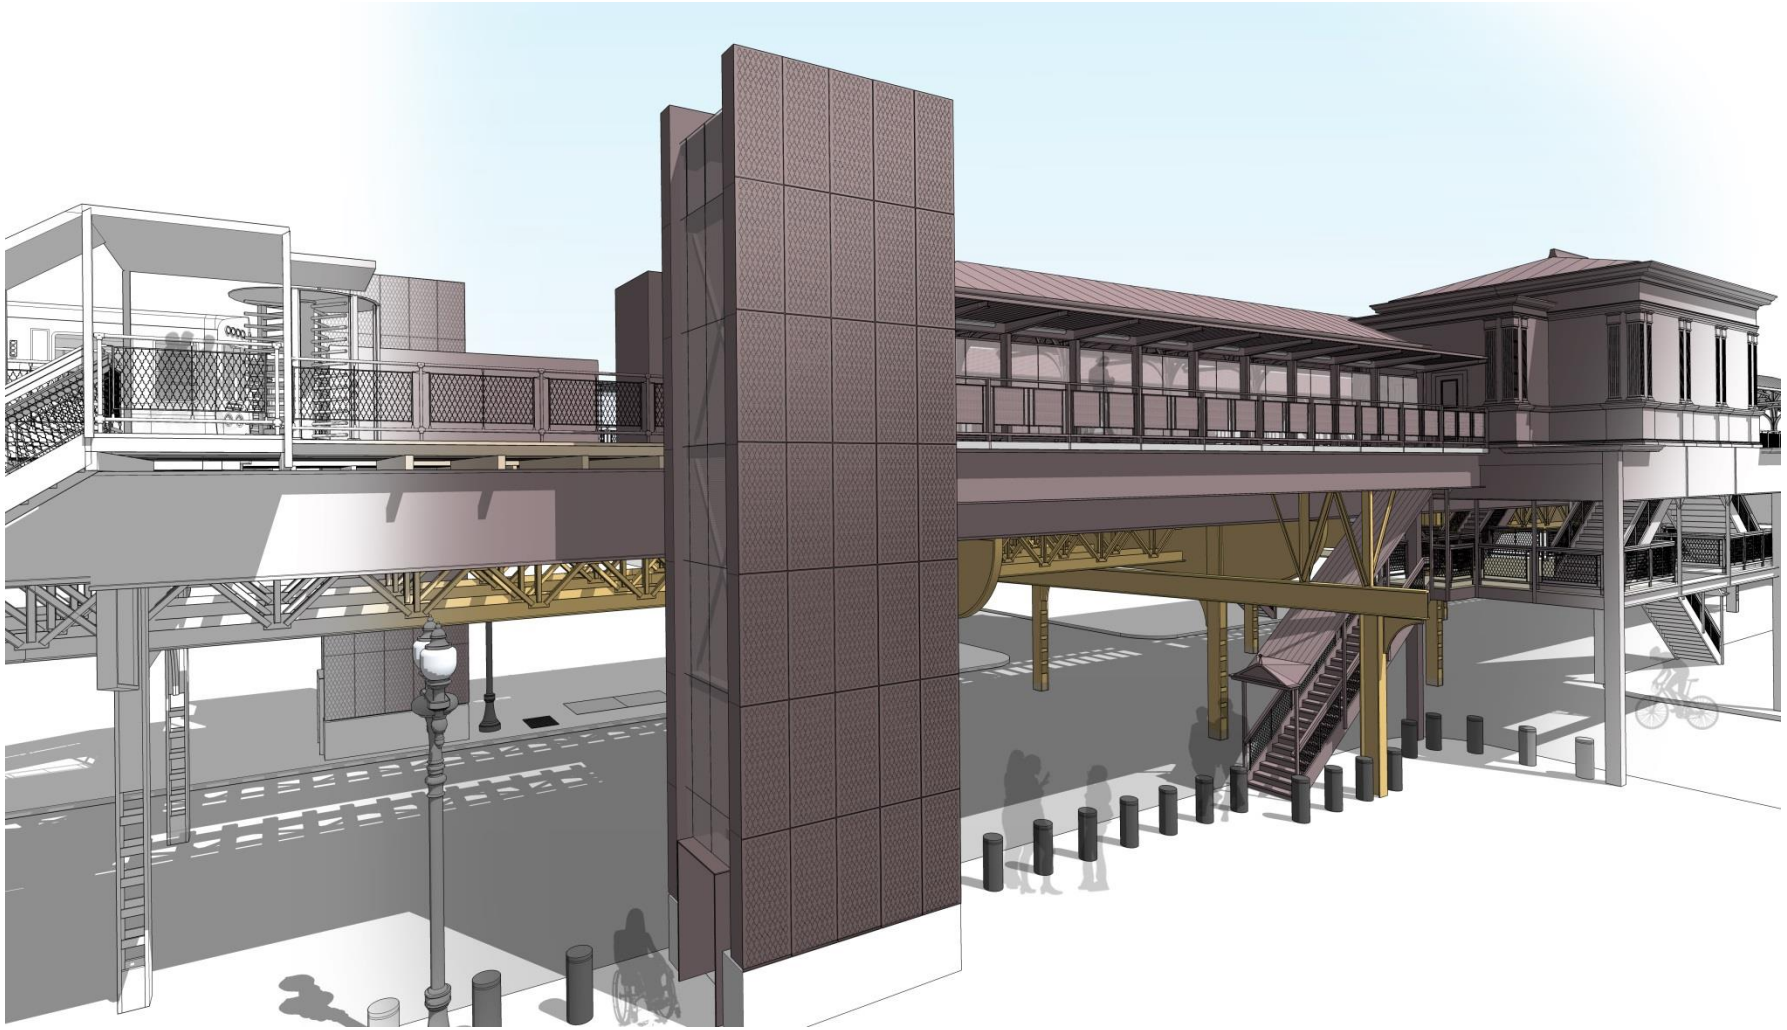

Quincy Rendering

